

Fundamentals of Software Project Management (SE4002)

Do not write below this line

Attempt all the questions on space provided on
paper.

Double sided, A4 sized, hand written cheat sheet is
allowed.

Ask for extra sheets for ruff work.

Date: June 4th 2026

Course Instructor(s)

Momna Zaneb (BSE-6A,BSE-
6B)

Final Exam

Total Time (Hrs): 3 hrs

Total Marks: 95

Total Questions: 5

58

Beentish

CLO 1: Explain principles of project life cycle.

Q1: Multiple Choice Questions — Circle the letter of the BEST answer.

[25 Marks]

16

No.	Question	Options
1	Which document formally authorizes a project and grants the project manager authority to apply organizational resources?	A) Project Management Plan B) Project Charter C) Scope Baseline D) Statement of Work
2	The process of subdividing project deliverables and work into smaller, more manageable components is called:	A) Activity Sequencing B) Work Breakdown Structure (WBS) C) Resource Leveling D) Rolling Wave Planning
3	In the project closing phase, the PRIMARY activity is:	A) Finalizing the project budget

National University of Computer and Emerging Sciences

Lahore Campus

		☒ B) Obtaining formal acceptance of deliverables and archiving records C) Updating the risk register D) Conducting performance reviews for team members
4	Which Scrum event is used to inspect the increment and adapt the product backlog if needed?	A) Sprint Planning B) Daily Scrum C) Sprint Review ☒ D) Sprint Retrospective
5	In Scrum, the 'Definition of Ready' (DoR) ensures that:	A) A product increment meets the agreed quality standard ☒ B) A user story is sufficiently clear before it enters a sprint C) The sprint backlog is fully estimated in hours D) The product owner has accepted the final release
6	Which Agile estimation technique uses relative sizing with a Fibonacci-like scale?	A) Function Point Analysis B) PERT Estimation C) Planning Poker ☒ D) COCOMO Model
7	A burndown chart in Scrum shows:	☒ A) Cost spent vs. cost planned over time B) Remaining work vs. time elapsed in a sprint C) Team velocity across multiple sprints D) Number of defects found per sprint
8	During risk identification, a RISK REGISTER typically records which of the following?	A) Budget allocations and resource assignments ☒ B) Risk description, probability, impact, and response strategy C) Stakeholder contact information and roles D) Quality metrics and acceptance criteria
9	Purchasing insurance for a software project is an example of which risk response strategy?	A) Avoid B) Mitigate C) Transfer ☒ D) Accept
10	Which of the following is a SECONDARY risk?	A) A risk that was not identified during planning ☒ B) A new risk created as a direct result of implementing a risk response C) A risk with a probability greater than 70% D) A risk that affects the critical path

National University of Computer and Emerging Sciences

Lahore Campus

		☒ B) Obtaining formal acceptance of deliverables and archiving records C) Updating the risk register D) Conducting performance reviews for team members
4	Which Scrum event is used to inspect the increment and adapt the product backlog if needed?	A) Sprint Planning B) Daily Scrum C) Sprint Review ☒ D) Sprint Retrospective
5	In Scrum, the 'Definition of Ready' (DoR) ensures that:	A) A product increment meets the agreed quality standard ☒ B) A user story is sufficiently clear before it enters a sprint C) The sprint backlog is fully estimated in hours D) The product owner has accepted the final release
6	Which Agile estimation technique uses relative sizing with a Fibonacci-like scale?	A) Function Point Analysis B) PERT Estimation C) Planning Poker ☒ D) COCOMO Model
7	A burndown chart in Scrum shows:	☒ A) Cost spent vs. cost planned over time B) Remaining work vs. time elapsed in a sprint C) Team velocity across multiple sprints D) Number of defects found per sprint
8	During risk identification, a RISK REGISTER typically records which of the following?	A) Budget allocations and resource assignments ☒ B) Risk description, probability, impact, and response strategy C) Stakeholder contact information and roles D) Quality metrics and acceptance criteria
9	Purchasing insurance for a software project is an example of which risk response strategy?	A) Avoid B) Mitigate C) Transfer ☒ D) Accept
10	Which of the following is a SECONDARY risk?	A) A risk that was not identified during planning ☒ B) A new risk created as a direct result of implementing a risk response C) A risk with a probability greater than 70% D) A risk that affects the critical path

National University of Computer and Emerging Sciences

Lahore Campus

11	Activity A has an optimistic duration of 4 days, most likely of 7 days, and pessimistic of 16 days. What is the PERT expected duration?	A) 7.0 days B) 7.67 days C) 8.0 days D) 9.0 days
12	Which of the following is a primary concern of Project Portfolio Management (PPM) rather than individual Project Management?	A) Monitoring the daily tasks of developers to ensure sprint goals are met B) Deciding how to allocate limited financial and staff resources across multiple competing projects C) Managing the internal scope changes of a single software module D) Defining the specific technical stack to be used by a project development team
13	Lag in project scheduling refers to:	A) The amount of time a task can be delayed without delaying the project B) A mandatory waiting period between two dependent activities C) Starting a successor activity before its predecessor finishes D) The difference between Early Finish and Late Finish
14	A project has BAC = £200,000, EV = £80,000, and AC = £100,000. What is the Cost Variance (CV)?	A) £20,000 B) -£20,000 C) £120,000 D) -£120,000
15	Schedule Performance Index (SPI) = 1.25 means the project is:	A) 25% over budget B) 25% behind schedule C) 25% ahead of schedule D) 25% under budget
16	Which cost estimation technique uses actual costs from previous similar projects as the basis for estimating the current project?	A) Parametric estimating B) Bottom-up estimating C) Analogous estimating D) Three-point estimating
17	A control chart is used in quality management primarily to:	A) Rank defect causes from most to least frequent B) Monitor process stability and detect when a process is out of control C) Map the steps in a process to identify bottlenecks D) Scatter-plot two quality variables to find correlation
18	Which cost of quality category includes peer reviews, walkthroughs, and software inspections?	A) External failure cost B) Internal failure cost C) Prevention cost D) Appraisal cost

National University of Computer and Emerging Sciences
Lahore Campus

19	ISO/IEC 25010 (SQuaRE) defines which of the following as a top-level software quality characteristic?	☒ A) Velocity ☐ B) Maintainability ☐ C) Burndown ☐ D) Story point
20	The 'cone of uncertainty' in software project management illustrates that:	☐ A) Estimates become less accurate as the project progresses ☐ B) Cost estimates are more reliable than schedule estimates ☒ C) Uncertainty in estimates decreases as the project progresses and more information is known ☐ D) Risk increases exponentially during execution
21	Which contract type places the GREATEST financial risk on the buyer (client)?	☐ A) Firm Fixed-Price (FFP) ☐ B) Fixed-Price Incentive Fee (FPIF) ☐ C) Cost Plus Fixed Fee (CPFF) ☒ D) Time and Material (T&M)
22	In configuration management, a 'baseline' is best described as:	☐ A) The original project budget before any changes ☒ B) A formally approved version of a configuration item that serves as the basis for future change ☐ C) The minimum acceptable quality level for a deliverable ☐ D) The project schedule at project kickoff
23	Earned Value (EV) is computed as:	☐ A) Actual Cost × Percent Complete ☒ B) Budget at Completion × Percent Complete ☐ C) Planned Value – Actual Cost ☐ D) Budget at Completion ÷ Cost Performance Index
24	Which of the following BEST describes velocity in an Agile project?	☐ A) The number of hours worked per sprint ☒ B) The average story points completed per sprint over time ☐ C) The rate at which defects are being introduced into the product ☐ D) The speed at which the product backlog is being groomed
25	In software quality, 'fitness for purpose' is most closely associated with which McCall quality factor?	☐ A) Maintainability ☐ B) Reliability ☒ C) Correctness ☐ D) Portability

National University of Computer and Emerging Sciences

Lahore Campus

CLO 2: Apply approaches to manage and optimize the software development processes.

Q2: TechForward Solutions has been awarded a contract to develop a Patient Management System (PMS) for a network of private hospitals. The system covers patient registration, appointment scheduling, billing, and electronic medical records. After delivery, the project manager Sara compiled the project data shown below: [20 marks]

#	Detail	Value
1	Total developer working hours logged across the entire project previous project 168 pages	12,400 hours
2	Total size of the delivered system	31 KLOC
3	System size measured in function points	620 FP
4	Lines of code reused from the previous Hospital Admin System	7,750 LOC (= 7.75 KLOC)
5	Total pages of documentation produced for the PMS	480 pages
6	Documentation pages adapted / reused from the previous project	168 pages

Sara must present a metrics report to hospital management to demonstrate team productivity and how effectively prior work was leveraged. The management are non-technical and need plain-language explanations alongside the numbers.

Choose appropriate metrics to calculate the required results. Interpret results in plain language. [4+8+8]

Metric	Calculation	Result interpretation
Working hours per Function Point	$= \frac{12\,400}{620} = 20 \text{ h/FP}$	20 developer hours were spent on completing each FP. Development team was rather Less productive given the code reuse ratio.
Code Reusability Percentage	$= \frac{7.75 \text{ KLOC}}{31 \text{ KLOC}} \times 100 = 25\%$	A quarter of the code was reused from previous projects. This shows significant code reuse.
Documentation Reusability Percentage	$= \frac{168 \text{ pages}}{480 \text{ pages}} \times 100 = 35\%$	35% documentation in this project was reused documentation from a previous project. Means significant portion of documentation was reused

National University of Computer and Emerging Sciences

Lahore Campus

--	--	--

CLO 2: Apply approaches to manage and optimize the software development processes.
Q3: Read the given scenario carefully & answer the questions.

[10 Marks]

Scenario: A software development firm is running four concurrent projects, each utilizing a different approach to coordinate group work:

- **Project Alpha:** The project manager asks five senior developers to independently estimate the total person-months required to build a new AI-driven module. The manager plans to average these individual inputs to determine the final project budget, allowing extreme over- or under-estimations to balance out.
- **Project Beta:** The development team is building a complex microservices architecture. Microservice 1, Microservice 2, and Microservice 3 must all be fully integrated and functional before the system can undergo final deployment. Development on Microservice 2 is severely bottlenecked because a junior developer is struggling with complex API integrations.
- **Project Gamma:** The QA department assigns a group of five testers to find critical, show-stopping security vulnerabilities in a new banking application. The testers operate independently within the codebase. The entire task is successful the moment at least one tester discovers a critical SQL injection flaw and the rest of the team confirms it is valid.
- **Project Delta:** To prepare for an upcoming data migration, a team of technical writers is assigned to manually clean up thousands of duplicate records in a spreadsheet. The team members work simultaneously, and each individual's hourly progress is directly combined to determine the total number of records cleaned by the end of the day.

3.1. Identify the specific group task category being utilized in Projects given below.

[8 Marks]

Project	Task Category & Justification
Alpha	<u>Compensatory</u> Since all individual inputs are averaged into one, the average gives the best estimate. This is a compensatory group task where extreme guesses compensate each other to push the average to the correct estimate.
Beta	<u>Conjunctive</u> Conjunctive group tasks move all together with the group. The slowest performer bottlenecks the entire group's outcome, which is the exact case of the junior developer described here.
Gamma	<u>Disjunctive</u> : Since testers operate independently, the entire group's performance is as good as the best tester. This is a case of disjunctive group tasks: more testers doesn't improve testing speed but better testers do.

National University of Computer and Emerging Sciences

Lahore Campus

Delta	<u>Additive</u> Additive group tasks are directly sped up with involvement of more people, like plain labour jobs. Since duplicate record removal will be done faster with more people, this is a case of additive group tasks.
-------	--

3.2. For Project Beta, what collaborative attitude or team behaviour should the project manager encourage to resolve the bottleneck? Cite the concept from your study text. [2 Marks]

If the Chief Programmer Team Structure is used, the junior can work on the better and stronger code standards instead of having to struggle with writing everything from scratch.

CLO 2: Apply approaches to manage and optimize the software development processes.

Q4: Apply the COCOMO Intermediate Model for Software Estimation.

[20 Marks]

Scenario:

A software development company has been contracted to build a nationwide online tax-filing system to be used by millions of citizens and thousands of tax officers simultaneously. The system must support secure multi-factor authentication, real-time tax computation, electronic document submission, automated audit flagging, and integration with existing government financial databases. Due to the highly sensitive nature of financial data, the system must operate with very high reliability and must handle extreme concurrent-user loads during filing deadlines.

The development team consists of analysts with high capability and programmers with nominal capability. The team has low prior experience with similar government-scale systems. The product complexity is very high, and the system must access and update a very large financial database. Modern development tools and environments will be used throughout. There are no extreme timing or memory hardware constraints. The estimated size of the system is 60,000 lines of code (60 KLOC).

Use the tables below to determine appropriate cocomo mode & cost driver ratings to apply the Intermediate COCOMO model.

Mode	A	b	c	d
Organic	2.4	1.05	2.5	0.38
<u>Semi-Detached</u>	3.0	1.12	2.5	0.35
Embedded	3.6	1.20	2.5	0.32

Cost Driver	Very Low	Low	Nominal	High	Very High	Extra High
RELY (Required reliability)	0.75	0.88	1.00	1.15	<u>1.40</u>	—
DATA (Database size)	—	0.94	1.00	1.08	<u>1.16</u>	—
CPLX (Product complexity)	0.70	0.85	1.00	1.15	<u>1.30</u>	1.65
TIME (Execution time constraint)	—	—	1.00	1.11	1.30	<u>1.66</u>

National University of Computer and Emerging Sciences Lahore Campus

STOR (Main storage constraint)	—	—	1.00	1.06	1.21	1.56
VIRT (Virtual machine volatility)	—	0.87	1.00	1.15	1.30	—
TURN (Computer turnaround time)	—	0.87	1.00	1.07	1.15	—
ACAP (Analyst capability)	1.46	1.19	1.00	0.86	0.71	—
AEXP (Application experience)	1.29	1.13	1.00	0.91	0.82	—
PCAP (Programmer capability)	1.42	1.17	1.00	0.86	0.70	—
VEXP (VM experience)	1.21	1.10	1.00	0.90	—	—
LEXP (Language experience)	1.14	1.07	1.00	0.95	—	—
MODP (Modern programming practices)	1.24	1.10	1.00	0.91	0.82	—
TOOL (Use of software tools)	1.24	1.10	1.00	0.91	0.83	—
SCED (Required development schedule)	1.23	1.08	1.00	1.04	1.10	—

4.1. Identify the appropriate COCOMO mode for this project and justify your choice. [2 Marks]
 Using Semi-Detached mode as there exists a mix of experienced and inexperienced team members, and the project complexity is very high.

4.2. Select cost driver ratings from the scenario. Calculate the Effort Adjustment Factor (EAF). Show all selected values.

Selected Cost Driver Ratings have been encircled in the table. (For unspecified Cost Driver Ratings, the Nominal 1.0 value is chosen) [6 Marks]

$$EAF = (1.40)(1.16)(1.30)(1.06)(0.86)(1)(0.91)$$

$$EAF = 2.7426 \quad EAF = 3.0992$$

4.3. Estimate total development effort in person-months using.

[6 Marks]

$$\text{Effort} = a(\text{KLOC})^b \times \text{EAF}$$

For semi-detached mode: $a=3.0$ $b=1.12$

$$= (3.0)(60)^{(1.12)} (3.0992)$$

~~Effort = 806.91 Person Months~~

Effort = 911.80 Person-Months

4.4. Estimate project duration (months).

[3 Marks]

$$T_{\text{dev}} = cE^d$$

For semi-detached mode: $c=2.5$ $d=0.35$

$$= (2.5)(911.80)^{0.35} = 27.15$$

~~$T_{\text{dev}} = 27.15$~~ Months

4.5 Estimate team size.

[3 Marks]

$$\text{Team Size} = N = E / T_{\text{dev}}$$

$$= \frac{911.80}{27.15} = 33.5837 \approx 34$$

Team Size = $N \approx 34$ Persons

CLO 2: Apply approaches to manage and optimize the software development processes.

Q5: Apply the Critical Path Method.

[20 Marks]

- A. Draw Activity on node graph. [10 Marks]
- B. Perform backward and forward pass [5 Marks]
- C. Highlight Critical Path. [2 Marks]
- D. Calculate Lag. [2 Marks]
- E. Find minimum project duration. [1 Marks]

Scenario:

NexaBank, a leading commercial bank, has commissioned a software development firm to build a **Digital Banking Platform (DBP)** that will offer customers online account management, fund transfers, loan applications, and a merchant payment gateway. The platform must go live before the annual peak transaction season. The project manager, **Hamza**, has broken the project into **12 activities**. The table below lists each activity, its duration in working days, its immediate predecessors, and the daily resource cost:



Momna Zaneb

Jun 11

I know you all prepared with the help of past papers , however the questions never appear same to same in any exam.

You had to dig in to find the twist in the given question.



Jun 11

Reasons why embedded mode was applicable to cocomo question:

Inflexible Operational Environment:

The fundamental definition of an Embedded system in COCOMO is one that operates within a tight set of operational constraints.

The Scenario Clue: The system must handle "extreme concurrent-user loads during filing deadlines."

The Reason: A tax deadline is legally non-negotiable. If the system crashes, slows down, or fails to compute taxes in real time on the final night of filing, it results in legal liabilities, public outcry, and government failure. This level of operational rigidity is the hallmark of Embedded software.

2. High Reliability and Data Sensitivity

The Scenario Clue: "Due to the highly sensitive nature of financial data, the system must operate with very high reliability..."

The Reason: In Organic or Semi-detached modes, a system crash is an inconvenience that can be patched in the next release with minimal damage. For a national financial database handling millions of citizens' personal wealth and multi-factor authentication, data corruption or system downtime is catastrophic. This dictates an Embedded classification where high reliability is structurally baked into the architectural design from day one.

3. Complex Hardware and Database Interfaces

The Scenario Clue: The system requires "integration with existing government financial databases" and must "access and update a very large financial database."

The Reason: Semi-detached systems typically operate with standalone or moderately coupled interfaces. A system that must concurrently process live calculations, cross-reference automated audit flags, and safely read/write to legacy government mainframes simultaneously requires complex multiplexing and highly intricate interface controls—fitting the Embedded mode perfectly


4. Rigid Requirements vs. Team Experience

The Scenario Clue: The team has "low prior experience with similar government-scale systems" and "programmers with nominal capability."

The Reason: In a Semi-detached mode, if a team lacks experience, the project scope or goals can often be negotiated or adjusted smoothly to match their pace. In Embedded mode, the goals cannot change. In given scenario The tax laws, security protocols, and integration points are fixed by state policy. The team must conform entirely to the rigid system requirements rather than the system conforming to the team's capabilities.

Activity	Description	Duration (days)	Predecessor(s)
A	Project planning & feasibility study	4	—
B	Requirements gathering & analysis	6	A
C	System architecture & design	5	A
D	Database design & setup	3	B
E	UI/UX prototyping & approval	4	B
F	Backend API development	8	C, D
G	Frontend development	6	C, E
H	Third-party integration (payments, SMS)	5	F
I	System testing & bug fixing	7	F, G
J	User acceptance testing (UAT)	4	H, I
K	Staff training & documentation	3	G
L	Deployment & go-live	2	J, K

A&B)

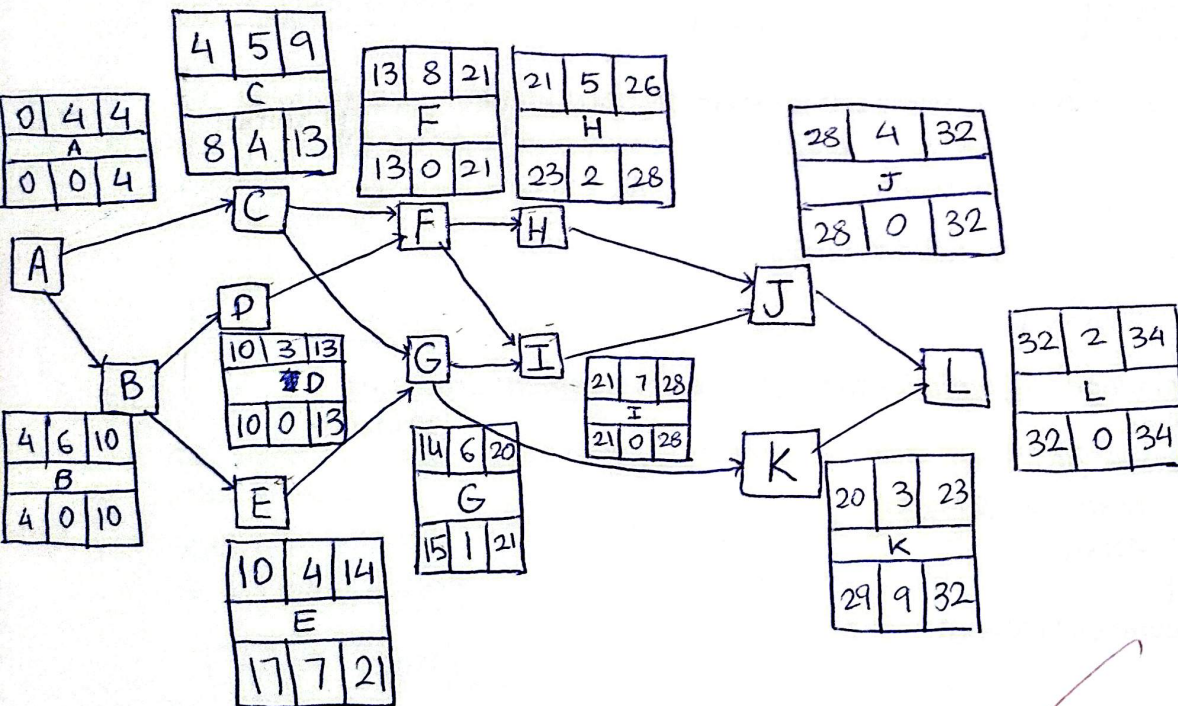

c) Critical Path : A → B → D → F → I → J → L

D) Total Lag (Slack Time) = 4 + 7 + 1 + 2 + 9

$$\text{Lag} = 23$$

E) Min. Proj duration = Earliest Finish of L = 34

Fundamentals of Software Project Management (SE4002)

Name = Hasan Yahya

Do not write below this line

Attempt all the questions on space provided on paper.

Double sided, A4 sized, hand written cheat sheet is allowed.

For ruff work, Take extra sheet from examiner.

22L-797H

Roll No

BSE-7B

Section

Date: Dec 26th 2025

Course Instructor(s)

Momna Zaneb (BSE-7A,
BSE-7B)

Javeria Sadiq (BSE-7C)

79

Final Exam

Total Time (Hrs):	3hrs
Total Marks:	100
Total Questions:	6

CLO2: Apply approaches to manage and optimize the software development processes

Question 1: Apply the Cocomo model for software estimation.

20 Marks

A software company has been assigned the task of developing a nationwide online examination system to be used by multiple universities simultaneously. The system will support secure student authentication, real-time online examinations, automatic and manual grading, and detailed audit logs for result verification. Due to the critical and sensitive nature of examination data, the software is expected to operate with high reliability and security and must be capable of handling thousands of concurrent users during peak examination periods. The application involves high processing and control complexity, along with a large database containing student

National University of Computer and Emerging Sciences Lahore Campus

records, examination papers, and results. The estimated size of the system, based on early design analysis, is approximately 80,000 lines of code.

The development team consists of analysts with average capability, while the programmers are highly skilled, although the team has limited prior experience with similar large-scale examination systems. Modern software development tools and environments will be used throughout the project. The system will be deployed on a standard hardware and software platform, without extreme memory, timing, or hardware constraints.

Based on the above information, students are required to estimate the development effort and schedule using the Intermediate COCOMO model.

Mode	a	b	c	d
Organic	2.4	1.05	2.5	0.38
Semi-Detached	3.0	1.12	2.5	0.35
Embedded	3.6	1.20	2.5	0.32

→ Used

Cost Driver	Very Low	Low	Nominal	High	Very High	Extra High
RELY (Required reliability)	0.75	0.88	1.00	1.15	1.40	—
DATA (Database size)	—	0.94	1.00	1.08	1.16	—
CPLX (Product complexity)	0.70	0.85	1.00	1.15	1.30	1.65
TIME (Execution time constraint)	—	—	1.00	1.11	1.30	1.66
STOR (Main storage constraint)	—	—	1.00	1.06	1.21	1.56
VIRT (Virtual machine volatility)	—	0.87	1.00	1.15	1.30	—
TURN (Computer turnaround time)	—	0.87	1.00	1.07	1.15	—
ACAP (Analyst capability)	1.46	1.19	1.00	0.86	0.71	—
AEXP (Application experience)	1.29	1.13	1.00	0.91	0.82	—
PCAP (Programmer capability)	1.42	1.17	1.00	0.86	0.70	—
VEXP (VM experience)	1.21	1.10	1.00	0.90	—	—
LEXP (Language experience)	1.14	1.07	1.00	0.95	—	—
MODP (Modern programming practices)	1.24	1.10	1.00	0.91	0.82	—
TOOL (Use of software tools)	1.24	1.10	1.00	0.91	0.83	—
SCED (Required development schedule)	1.23	1.08	1.00	1.04	1.10	—

1. Estimate the total development effort. Show complete working.

$$EAF = 1 \times 0.91 \times 1 \times 1 \times 1 \times 0.86 \times 1.13 \times 1 \times 1 \times 1 \times 1 \times 1.15 \times 1.08 \times 1.15 = 1.26309965$$

As, it is 80,000 lines of code and significant non-functional constraints as well as nominal experience. Not a lot of experience) Semi-detached model (complexity is high but not very high);

$$\begin{aligned} \text{Effort} &= a(\text{Size})^b \times EAF \\ &= 3(80)^{1.12} \times 1.26309965 \\ &= 512.8847231 \text{ person months} \end{aligned}$$

2. Estimate the development time.

6 marks

$$T_{dev} = c E^d = 2.5 (512.8847)^{0.35} = 22.2048 \text{ months.}$$

3. Estimate the team size.

4 marks

$$N \geq E / T_{dev} = \frac{512.8847}{22.2048} = 23.097 \text{ persons.}$$

CLO1: Understand project management principles and techniques

Question 2: Write the most appropriate quality factor for each requirement.

(20 Marks)

The software requirement document for the tender for development of "Super-lab", a software system for managing a hospital laboratory, consists of chapters according to the required quality factors as follows: correctness, reliability, efficiency, integrity, usability, maintainability, flexibility, testability, portability, reusability and interoperability. In the following table you will find sections taken from the mentioned requirements document. For each section, fill in the name of the factor that best fits the requirement (choose only one factor per requirements section).

No	Requirement	Quality Factor
1	The probability that the "Super-lab" software system will be found in a state of failure during peak hours (9 am to 4 pm) is required to be below 0.5%.	Reliability
2	The "Super-lab" software system will enable direct transfer of laboratory results to those files of hospitalized patients managed by the "MD-File" software package.	Interoperability
3	The "Super-lab" software system will include a module that prepares a detailed report of the patient's laboratory test results during his or her current hospitalization. (This report will serve as an appendix to the family physician's file.) The time required to obtain this printed report will be less than 60 seconds; the level of accuracy and completeness will be at least 99%.	Efficiency
4	The "Super-lab" software to be developed for hospital laboratory use may be adapted later for private laboratory use.	Flexibility
5	The training of a laboratory technician, requiring no more than three days, will enable the technician to reach level C of "Super-lab" software usage. This means that he or she will be able to manage reception of 20 patients per hour.	Usability
6	The "Super-lab" software system will record a detailed users' log. In addition, the system will report attempts by unauthorized persons to obtain medical information from the	Integrity

National University of Computer and Emerging Sciences
Lahore Campus

laboratory test results database. The report will include the following information: network identification of the applying terminal, system code of the employee who requested that information, day and time of attempt, and type of attempt.	Integrity
The "Super-lab" subsystem that deals with billing patients for their tests may eventually be used as a subsystem in the "Physiotherapy Center" software package.	Reusability
The "Super-lab" software system will process all the monthly reports for the hospital departments' management, the hospital management, and the hospital controller according to Appendix D of the development contract.	Correctness
The software system should be able to serve 12 work stations and eight automatic testing machines with a single model AS20 server and a CS25 communication server that will be able to serve 25 communication lines. This hardware system should conform to all availability requirements as listed in Appendix C	Interoperability Testability
The "Super-lab" software package developed for the Linux operating system should be compatible for applications in a Windows NT environment.	Portability

CLO1: Understand project management principles and techniques

Question 3: Read the items given in Column A and choose most appropriate option from Column B. Write the chosen option(number only) in column C. Overwriting or cutting will result in loss of marks

(20 Marks)

No	A	B	C
1	ISO 9126	1B. One codes while the other reviews work in pairs	13B
2	CMMI	2B. Functionality enhancement	12B
3	Developers work in pairs	3B. RFP	1B
4	Sprint	4B. Product Transition	16B
5	Mc Calls	5B. Version	15B
6	Flexibility	6B. Integrity	7B
7	Interoperability	7B. Revision	4B
8	Product Operation	8B. Risks	6B
9	Hawthorne Effect	9B.CPM	14B
10	Configuration that existed at certain point in time	10B.Hazards	18B
11	Numbering scheme that is used to identify the state of the configuration item at any time	11B. Pert	5B

12	SVN	12B. developed by the SEI	19B
13	A method that assumes deterministic times	13B. 1977	9B
14	A method that does not assume fixed durations.	14B. Productivity Increased	11B
15	Some are threats (bad) and some are opportunities (good).	15B. Good quality Software	10B
16	The situational factors that increase chances of bad outcomes	16B. Planned activity	8B
17	What you planned to have	17B. BCWS	2B
18	A written agreement between customer and supplier	18B. Time boxed	17B
19	A Document a company makes when it needs outside help	19B. SCM Tool	20B
20	Project	20B. SOW	3B

CLO1: Understand project management principles and techniques

Question 4: Mark the given statements True/False. Overwriting cutting will result in deduction of marks.

(20 Marks)

No.	Statement	True/False
1	Plan is a general way of doing a task (e.g., software testing).	F
2	Groups of methods/techniques is called Methodology	T
3	Bespoke System (Custom-built) is Built from scratch for one customer only	B T
4	Fixed Price Contract does not Agree cost set in advance	F
5	In Wideband Delphi, estimates are given openly in front of the group	F
6	Online queries are included when counting user inputs in the function point method. <i>(yes in external queries & interfaces)</i>	T
7	Function points are less dependent on programming language and developer coding style than KLOC.	T
8	Corrective maintenance services involve fixing failures detected either by customers or the service team.	T
9	Most customer calls to the software support center are expected to be failure-related.	T
10	Product metrics are related to the software development process	F

National University of Computer and Emerging Sciences Lahore Campus

It doesn't auto when, only auto it.

11	Paying developers early and receiving savings later is an example of cash flow issues.	T /
12	Net profit considers when the income and costs occur during the project.	F /
13	Payback period is simple to calculate but limited in long-term analysis.	T /
14	Net profit, ROI, and payback period all consider the timing of cash flows	F /
15	Both the Post-Architecture and Early Design models use the same functional form to estimate the amount of effort and calendar time it will take to develop a software project.	T /
16	The subscript NS in PMNS and TDEVNS represents non-standard schedule estimates.	T L
17	COCOMO II expresses size only in thousands of source lines of code (KSLOC).	T L
18	Story Points measure the absolute time required to complete a task.	F /
19	Velocity is calculated as the total number of tasks completed per sprint.	T L
20	Using a higher discount rate adjusts NPV for risky projects.	F L

taken no. of story points per sprint

CLO2: Apply approaches to manage and optimize the software development processes

Question 5: A software company developed a hospital management system over a period of eight months. To monitor progress, the project team defined eight major milestones corresponding to key development activities. At the end of the project, management observed that five milestones were completed on their scheduled dates, while the remaining milestones were completed late. When the delays were analysed, it was found that the total accumulated delay across all milestones was 16 days. During quality assurance activities, errors detected throughout the project were classified based on their origin and severity. Each error was assigned a numerical severity weight according to its impact on system operation. The analysis revealed that, Errors originating from coding activities had a total severity weight of 96, distributed across 24 individual code errors. Errors originating from earlier development activities such as requirements analysis and design had a total severity weight of 140, distributed across 28 development-related errors. With the help of provided data, apply suitable metrics to evaluate the project's performance.

- a. List down appropriate metrics applicable to this scenario.

(10 Marks)

*TTO, ADMS, ASCA, ASDE ie Timetable
& Error severity (Process Metrics)*

2 marks

- b. Apply Metrics to the data and show results.

8 marks

Metric Name	Metric Formula	Calculations
<i>Time Table Difference</i>	<i>TTO = MSOT / MS</i>	<i>TTO = 5 / 8 = 0.625</i>

which is 1, then, milestone are behind schedule.

Average delay of Milestone completion	$ADMS = TCDAM / MS$	$ADMS = 16/8 = 2$
Average severity of code errors	$ASCE = WCE / NCE$	$ASCE = 96/24 = 4$
Average severity of development errors	$ASDE = WDE / NDE$	$ASDE = 140/28 = 5$
Time table observance	$TTO = MSOT / MS$	$TTO = 5/8 = 0.625$

CLO2: Apply approaches to manage and optimize the software development processes

Question 6: A multinational e-commerce company is reviewing its customer order and inventory management system due to uncertainty in future growth caused by rapidly changing consumer demand and emerging competitors. Management estimates that there is a 30% chance the market will expand rapidly over the next three years, while a 70% chance exists that growth will remain moderate. The company is considering three strategic options. One option is to maintain the existing system, which would perform adequately and generate a net present value of £120,000 if growth is moderate, but would become overloaded and result in a loss of £200,000 if the market expands rapidly. Another option is to upgrade the system incrementally in two phases: the first phase requires immediate investment, after which management can decide whether to proceed to a second phase based on observed market conditions. If growth remains moderate after Phase 1, the system will perform well and deliver £180,000, but if growth is rapid, management must choose to either proceed with Phase 2, yielding £260,000, or stop further investment, yielding £40,000. The third option is to replace the system immediately, which would allow aggressive scaling and produce £350,000 if the market expands rapidly, but would be underutilized and result in a loss of £80,000 if growth is moderate.

(10 marks)

a. Calculate expected monetary values for each option.

3 marks

1- Maintain:

$$= (0.7 \times 120,000) + (0.3 \times -200,000) = 24,000 \$$$

3- Replace:

$$= (0.3 \times 350,000) + (0.7 \times -80,000) = 49,000 \$$$

2- Upgrade:
 if proceeds = $(0.3 \times 260,000) + (0.7 \times 180,000) = 204,000 \$$
 if stops = $(0.3 \times 40,000) + (0.7 \times 180,000) = 138,000 \$$

Fall 2025


Department of Software Engineering

Page 7 of 8

For the whole upgrade choice we use max of both ie $(0.3 \times 260,000) + (0.7 \times 180,000) = 204,000 \$$

→ In this case we say both proceed & stop are equally likely.

- b. Considering these uncertainties and potential outcomes, perform sensitivity analysis using decision tree. 5 marks

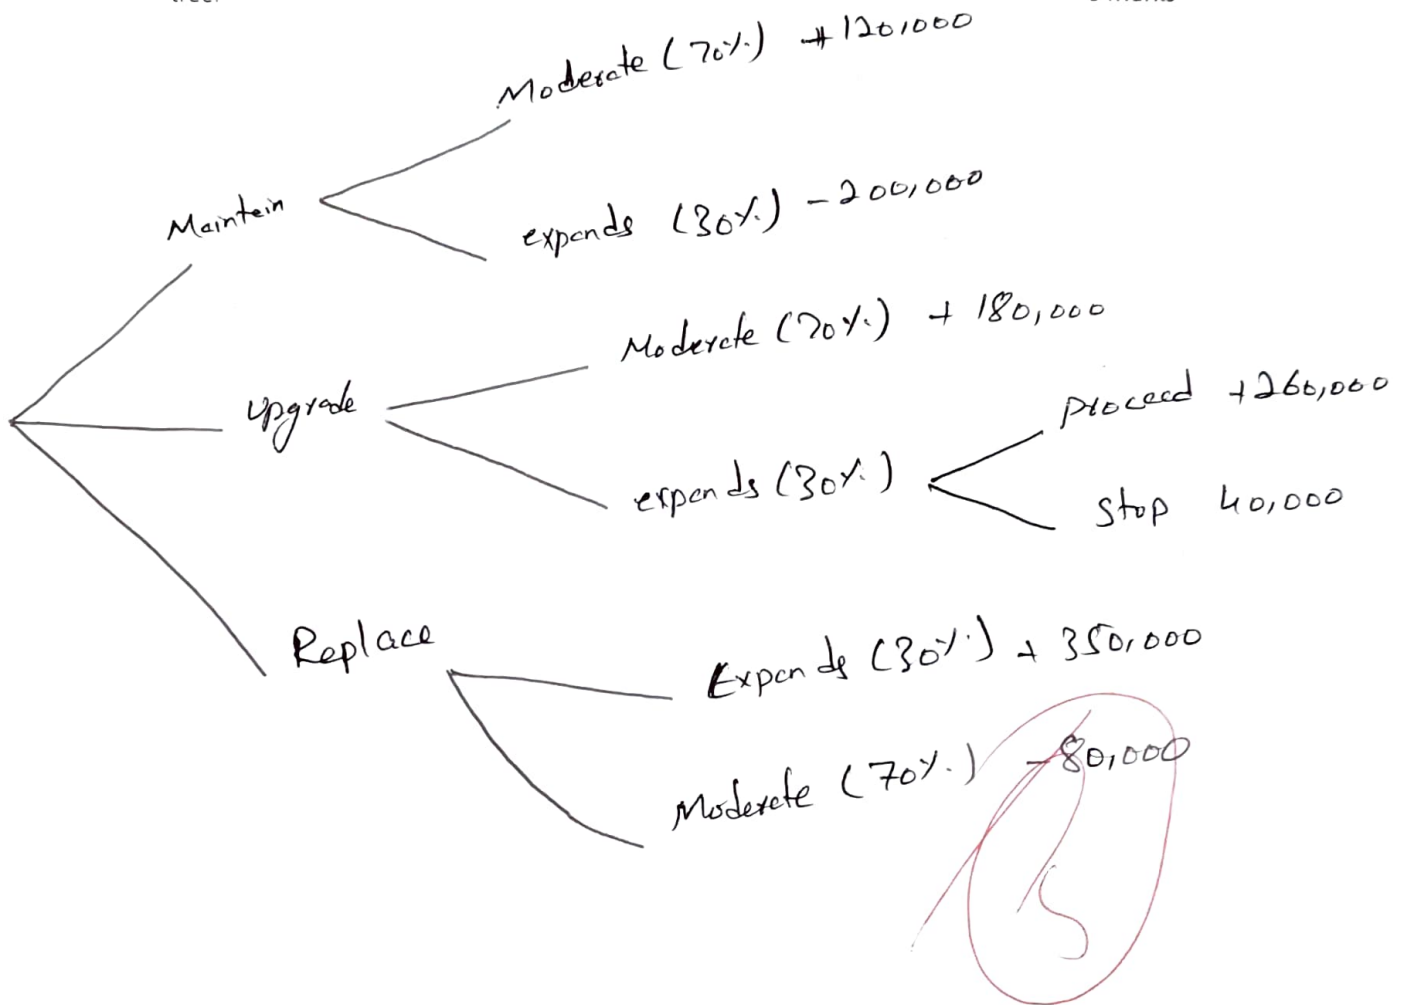

- c. Determine most suitable option based on results of sensitivity analysis and EMV. 2 marks

Based of the above information, user should upgrade (& ~~expand~~ in case of proceed in case of rapid expansion to Phase 2).

2

FSPM (SE4003)

Date: December 24th
2024

Course Instructor(s)

Ms. Momna Zainab

Mr. Salman Ahmad

Do not write below this line

Attempt all the questions.

Students are allowed to bring a A4 sized, handwritten, double-sided cheat-sheet to exam.

Final Exam

Total Time (Hrs): **3**

Total Marks: **95**

Total Questions: **6**

Section

Student Signature

Printed , and photocopied sheets are not allowed.

Question 5 & 6 are for Section B only.

Question 4 is for Section A only. Attempt Question 4 on question paper ONLY.

CLO 4: Apply approaches to manage and optimize the

software development processes

Q1: We as a software company have been awarded a maintenance project. Initially, we are required to determine if the continued maintenance of the software application under maintenance is affordable anymore. During this phase, our step will be to determine the cost of fixing defects by performing three activities. The first is to design and execute usage scenarios to determine if the application breaks too often during regular use. The second is to design and execute test cases to uncover faults in the application. The third is to remove the faults to see how long it takes to repair the application. The second step will be to modify existing features to determine if the cost of the changes is affordable or not. During this step, we shall modify the existing features and extend the functionality of the application by adding new features to determine the effort required to modify and add new functionality. After the first two steps, an analysis will be performed and it will be decided if the software application should remain in maintenance as before or it should be re-engineered. The first phase will run for 3 months. In the second phase, if the reengineering-related decision has been made, the foremost step of business process reengineering will be performed. This step will define the business goals, identify existing business processes, evaluate the existing processes, and create revised business processes. The second step will be the reengineering of software. This step will include activities such as inventory analysis, document restructuring, reverse engineering, program restructuring, data restructuring, and forward engineering. The third step will be to assess the quality of the resultant software and measure the maintainability of the resultant software.

- a. Someone has told us that having a Work Breakdown Structure (WBS) will help us execute the project better. We have also been told that students at FAST Lahore are very good at making WBS to help managers of software projects. Assuming that the decision after phase 1 will be to go for reengineering, provide a WBS for the phases mentioned above to help our company. As an incentive, you'll be awarded good marks if the WBS helps. Use a tree-like structure to show your WBS

10 marks

National University of Computer and Emerging Sciences

Lahore Campus

- b. A team of software engineers is working on a project following Scrum. At the start of each sprint, they select a few user stories to work on. Their selected and completed user stories in the first five sprints are as follows: **10 marks**

Sprint 1: The team committed to completing 8 user stories. However, the team could complete 6 of the 8 user stories. Out of those six stories, two stories had 10 story points, three stories had 5 story points, and one story had 3 story points.

Sprint 2: The team committed 10 user stories and completed 9 of the 10 user stories. Out of those nine stories, three stories had 2 story points, four stories had 6 story points, and two stories had 8 story points.

Sprint 3: The team committed 12 user stories and completed 10 of the twelve user stories. All ten user stories had 7 story points.

Sprint 4: The team committed 14 user stories and completed 12 of the 14 user stories. Out of those twelve user stories, six stories had 9 story points, four stories had 5 story points, and two stories had 3 story points.

Sprint 5: The team committed 15 user stories and completed 13 of the 15 user stories. Out of those thirteen user stories, five stories had 10 story points, four stories had 6 story points, and four stories had 2 story points.

1. Calculate the average sprint velocity based on how many story points are implemented in each sprint.
2. Calculate the total number of story points committed and the total number of story points completed for all five sprints.
3. Give the estimated story points the team should commit for Sprint 6.

CLO 4: Apply approaches to manage and optimize the software development processes

Q2: Your software house has signed a new project with Islamic organization to develop a mobile application named Eat-Halal. The application is to be used in the region of Europe.

System will provide following major functionalities:

1. Differentiate between Halal and Haram products
2. Generate smart suggestions of alternative halal products for a product identified as haram by the system.
3. Locate halal food places based on the user's location.
4. Generate smart suggestions for halal eating based on the user's interest and added preferences.

Eat-Halal shall use front end scraping to retrieve ingredient status from Islamic fatwa.com. If a website declares a food ingredient as haram the product will be declared as haram by our application. Machine learning technique "Bayesian classifier" will be used to get alternative options from other food websites. An AI based smart recommender system will be used for generating smart suggestions for halal eating. All the members of the team are experienced with phone application development, however, working with machine learning algorithms is a completely new & challenging task for them. Average monthly salary of team members is 80k. Estimated KLOC for the project is 35k.

National University of Computer and Emerging Sciences

Lahore Campus

Software Projects	A	B	C	D
Organic	2.4	1.05	2.5	0.38
Semi-Detached	3.0	1.12	2.5	0.35
Embedded	3.6	1.20	2.5	0.32

Read above mentioned information carefully and apply the suitable cocomo model to answer the following questions.

- Compute the Effort (in person-months) for the given project. **5 marks**
- Compute Time (in months) required to develop this project. **5 marks**
- Compute the number of team members required to develop the project. **5 marks**
- Compute estimated total cost of the project. **5 marks**

CLO 4: Apply approaches to manage and optimize the software development processes

Q3: Using earned value management system track the performance of the project.

You are managing a software development project with a total budget of \$400,000 and a planned duration of 5 months. At the end of Month 3, the following information is available:

- By the end of Month 3, the project was planned to have completed 70% of the total work.
- The actual work completed so far corresponds to 60% of the total project.
- The actual costs incurred to date are \$250,000.

Additionally, the project involves the following key tasks:

Task	Estimated Effort (Planned Hours)	Actual Effort (Hours)	Work Completed (%)
1	100	110	100%
2	150	140	90%
3	200	220	50%
4	120	130	80%
5	80	70	100%

To Do:

- Calculate the following Earned Value Management metrics: **10 marks**
 - Schedule Variance (SV) (Task & Project Level)**
 - Cost Performance Index (CPI) (Project Level)**
- Based on your calculations: **5 marks**
 - Assess whether the project is ahead or behind schedule.
 - Determine if the project is cost-efficient or inefficient.

National University of Computer and Emerging Sciences

Lahore Campus

CLO 1: Understand project management principles and techniques

Q4: Provide the correct answers for following questions. (For section A only)

A. Choose the correct personality type for each person i.e. ISFJ, INFJ.

10 marks

Person Profile	Personality Type
A scientist who spends hours formulating theories and exploring complex ideas in physics.	
A party host who keeps everyone entertained with humor, music, and spontaneous activities.	
A nurse who goes above and beyond to provide compassionate care for patients.	
A community leader who inspires others to join a cause and works tirelessly to achieve collective Goals.	
A meticulous accountant who ensures all financial records are precise and deadlines are always met.	

B. Correctly identify the stages of team formation.

10 marks

Description	Stage
Control established over resistance. A cohesive set of rules and standards is developed in the group.	
The purpose of the group is fulfilled.	
What the team will be doing? Interpersonal and task relationships are characterized by courtesy , confusion and caution.	
Members showing resistance. Lots of ongoing tension, criticism and confrontation.	
Group is focused on the task accomplishment. Issues of interpersonal relations, member status & division of task are settled.	

C. Fill in the blanks.

10 marks

- Team members that are under the direct managerial control of the project leader are called _____.
- Criteria of project success lies within the range of three constraints _____, _____, _____.
- ISO 9126 identifies _____ major external software quality characteristics.
- _____ refers to the ability of the software to share resources with other software components; unlike 'interoperability', no direct data passing is necessarily involved.
- risk exposure = (_____) x (probability of occurrence).

National University of Computer and Emerging Sciences

Lahore Campus

- f. The _____ defines the specification and constructs the high-level design, and then partitions the remaining tasks of detailed design, viz., coding, testing, documentation, etc., into many smaller tasks, and assigns them to the team members.
- g. _____ and _____ are the advantages of a fixed price contract.
- h. Oldham and Hackman suggest that the satisfaction that a job gives is based on _____ factors.
- i. The _____ is skilled at creating a good working environment, for example, by 'jolly'ing people along'.
- j. McCall's factor model classifies all software requirements into _____ software quality factors.

D. The software requirement document for the tender for development of "Super-lab", a software system for managing a hospital laboratory, consists of chapters according to the required quality factors as follows: correctness, reliability, efficiency, integrity, usability, maintainability, flexibility, testability, portability, reusability and interoperability. In the following table you will find sections taken from the mentioned requirements document. For each section, write the name of the factor that best fits the requirement (choose only one factor per requirements section). 10 marks

Requirement	Quality Factor
1. The probability that the "Super-lab" software system will be found in a state of failure during peak hours (9 am to 4 pm) is required to be below 0.5%.	
2. The "Super-lab" software system will enable direct transfer of laboratory results to those files of hospitalized patients managed by the "MD-File" software package.	
3. The "Super-lab" software system will include a module that prepares a detailed report of the patient's laboratory test results during his or her current hospitalization. (This report will serve as an appendix to the family physician's file.) The time required to obtain this printed report will be less than 60 seconds; the level of accuracy and completeness will be at least 99%.	
4. The "Super-lab" software to be developed for hospital laboratory use may be adapted later for private laboratory use.	
5. The training of a laboratory technician, requiring no more than three days, will enable the technician to reach level C of "Super-lab" software usage. This means that he or she will be able to manage reception of 20 patients per hour.	
6. The "Super-lab" software system will record a detailed users' log. In addition, the system will report attempts by unauthorized persons to obtain medical information from the laboratory test results database. The report will include the following information: network identification of the applying terminal, system code of the employee who requested that information, day and time of attempt, and type of attempt.	

National University of Computer and Emerging Sciences

Lahore Campus

7. The “Super-lab” software system will process all the monthly reports for the hospital department’s management, the hospital management, and the hospital controller according to Appendix D of the development contract.	
8. The software system should be able to serve 12 workstations and eight automatic testing machines with a single model AS20 server and a CS25 communication server that will be able to serve 25 communication lines. This hardware system should conform to all availability requirements as listed in Appendix C.	
9. The “Super-lab” software package developed for the Linux operating system should be compatible for applications in a Windows NT environment.	
10. The “Super-lab” subsystem that deals with billing patients for their tests may eventually be used as a subsystem in the “Physiotherapy Center” software package.	

CLO 1: Understand project management principles and techniques

Q5: Answer the following questions (For Section B)

- a. What do you mean by the characteristics of invisibility and complexity of Software project management? **5 marks**
- b. Define risk identification and ranking. **5 marks**
- c. Mention the important causes of stress encountered in projects. **5 marks**
- d. Briefly explain the different phases of project management life cycle using an illustration **5 marks**
- e. What is the difference between verification and validation and how does it help in software quality **5 marks**
- f. What are different choices of risk planning after having identified risks? Describe them briefly. **5 marks**

CLO# 4 Apply approaches to manage and optimize the software development processes

Q6: You have to manage a project with activities and their respective durations as listed in table below (For Section B only)

Activity	Immediate Predecessor	Duration (months)
A	-	2
B	A	4
C	A	2
D	B	2
E	B, C	4

National University of Computer and Emerging Sciences
Lahore Campus

F	A, E	6
G	D	4
H	D, E, F	2
I	G, H	6
J	H, F	6
K	H, I, J	4

- | | |
|--|---------|
| a. Construct Precedence diagram to analyse your project | 6 marks |
| a. What is the project duration | 1 mark |
| a. What are the critical activities | 1 mark |
| a. Show/Highlight critical path on your precedence diagram | 1 mark |
| a. When is the earliest D activity can possibly be completed | 1 mark |
